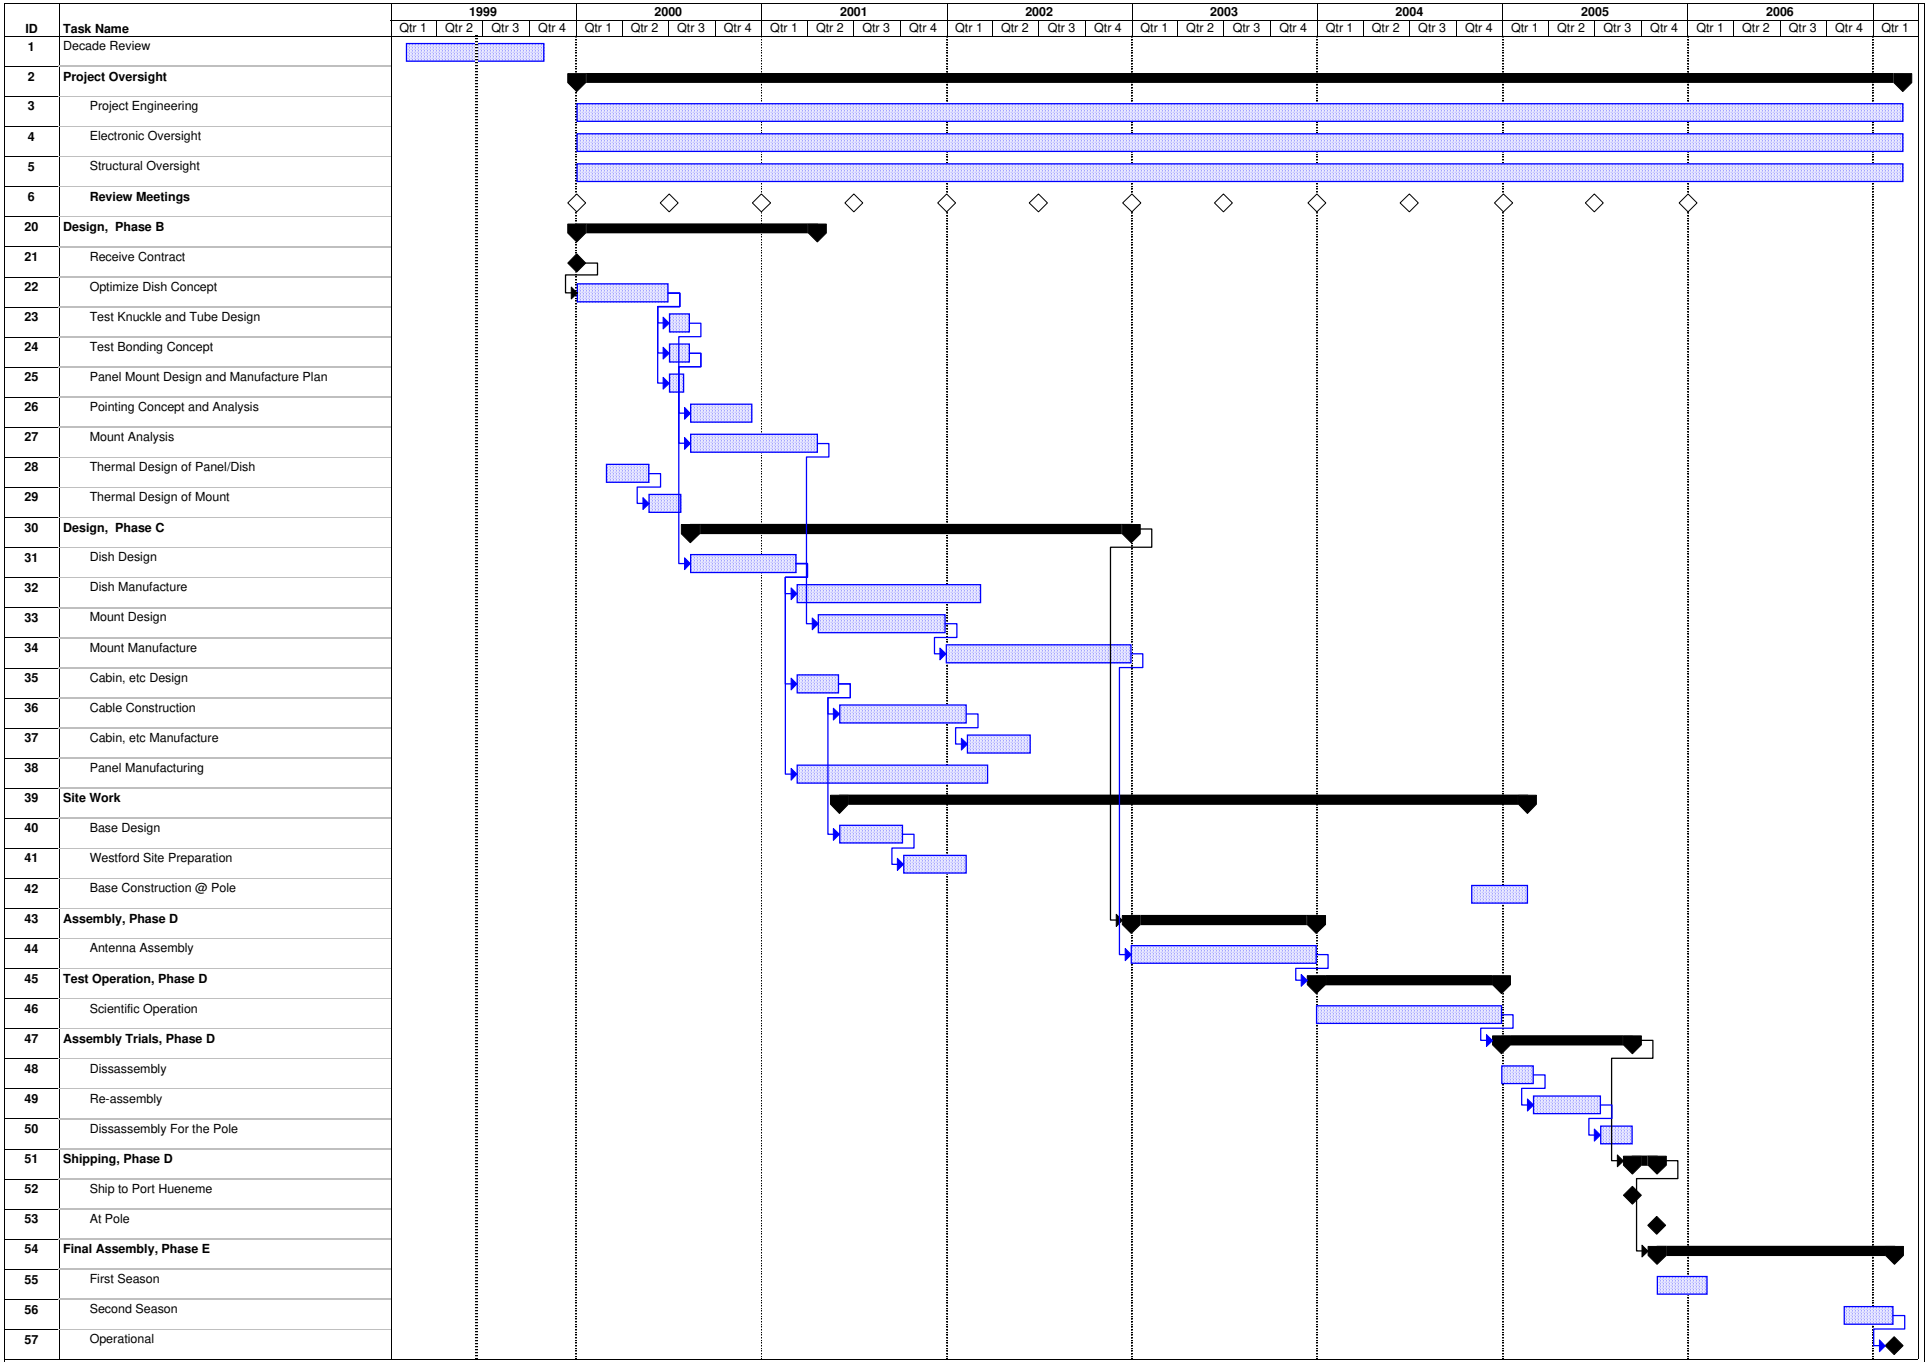

ID	Task Name
1	Decade Review
2	**Project Oversight**
3	Project Engineering
4	Electronic Oversight
5	Structural Oversight
6	**Review Meetings**
20	**Design, Phase B**
21	Receive Contract
22	Optimize Dish Concept
23	Test Knuckle and Tube Design
24	Test Bonding Concept
25	Panel Mount Design and Manufacture Plan
26	Pointing Concept and Analysis
27	Mount Analysis
28	Thermal Design of Panel/Dish
29	Thermal Design of Mount
30	**Design, Phase C**
31	Dish Design
32	Dish Manufacture
33	Mount Design
34	Mount Manufacture
35	Cabin, etc Design
36	Cable Construction
37	Cabin, etc Manufacture
38	Panel Manufacturing
39	**Site Work**
40	Base Design
41	Westford Site Preparation
42	Base Construction @ Pole
43	**Assembly, Phase D**
44	Antenna Assembly
45	**Test Operation, Phase D**
46	Scientific Operation
47	**Assembly Trials, Phase D**
48	Dissassembly
49	Re-assembly
50	Dissassembly For the Pole
51	**Shipping, Phase D**
52	Ship to Port Hueneme
53	At Pole
54	**Final Assembly, Phase E**
55	First Season
56	Second Season
57	Operational
